EAST TENNESSEE NATURAL GAS, LLC
915 North Eldridge Parkway, Suite 1100
Houston, Texas 77079
(713) 627-5400

ENBRIDGE

October 22, 2026

Ms. Debbie-Anne A. Reese, Secretary
Federal Energy Regulatory Commission
888 First Street, NE
Washington, DC 20426

Re: *East Tennessee Natural Gas, LLC*
Ridgeline Expansion Project, Docket Nos. CP23-516-000 and CP23-516-001
In-Service Request

Dear Ms. Reese:

On April 2, 2025, the Federal Energy Regulatory Commission ("FERC" or "Commission") issued an Order Issuing Certificate ("April 2 Order") in the above-referenced dockets granting East Tennessee Natural Gas, LLC ("East Tennessee") the authority to construct and operate the Ridgeline Expansion Project ("Project").[1] On October 7, 2025, the Commission authorized East Tennessee to commence Project construction activities.[2] Pursuant to Environmental Condition No. 11 of the April 2 Order, East Tennessee hereby requests that the Director of the Office of Energy Projects ("OEP") grant East Tennessee written authorization to place all of the Project facilities into service by November 1, 2026, as described more fully below.

Mechanical completion of all the Project facilities is anticipated to be achieved by October 23, 2026. East Tennessee confirms that it has met all of the conditions of the April 2 Order required to place the Project facilities into service and affirms that rehabilitation and restoration of the areas affected by the Project are proceeding satisfactorily. Project seeding and mulching is anticipated to be completed in November 2026. Progress of construction activities is attached as Attachment A hereto. Additionally, East Tennessee provides in Attachment B photos documenting rehabilitation and restoration of the areas affected by the Project.

East Tennessee is committed to maintaining sufficient restoration and environmental crews including environmental inspectors for both spreads after the Project is in-service and until the rehabilitation and restoration is complete. Attached hereto as Attachment C, East Tennessee provides its Restoration and Post-Construction Monitoring Plan and a table detailing the current status and estimated completion dates of rehabilitation and restoration of the Project, which outlines the measures East Tennessee will implement to complete rehabilitation and restoration of the Project facilities.

[1] *East Tennessee Natural Gas, LLC*, 191 FERC ¶ 61,004 (2025).
[2] *East Tennessee Natural Gas, LLC*, Notice to Proceed with Construction, Docket Nos. CP23-516-000 and CP23-516-001 (Oct. 7, 2025).

To date, East Tennessee has resolved all non-compliance matters with FERC and the Tennessee Department of Environment and Conservation and there are no other pending compliance matters with any other federal or state agency.[3] Additionally, East Tennessee has resolved or is in the process of resolving all landowner complaints to date and will remain committed to resolving any landowner related concerns or complaints related to the Ridgeline Expansion Project if any are received during the remainder of the Project. East Tennessee provides in Attachment D hereto a list of the remaining unresolved landowner issues, together with the applicable resolution plans and anticipated resolution dates.

East Tennessee requests that the Director of OEP grant the requested authorization for the Project facilities by October 28, 2026, so East Tennessee can place these facilities into service by November 1, 2026.

If you have any questions regarding this filing, please contact Anish George, Manager, Regulatory at (713) 627-5120 or the undersigned at (713) 627-4522.

Respectfully submitted,

/s/ *Estela D. Lozano*
Estela D. Lozano
Director, Regulatory

Attachment

cc: Brad Wazaney (FERC)
Tina Lyons (Burns & McDonnell)

[3] While East Tennessee has no outstanding non-compliance matters with the Tennessee Wildlife Resources Agency ("TWRA"), it is possible that TWRA may impose remedial measures at a future date regarding an issue at Hurricane Creek.

ATTACHMENT A

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Progress of Construction Activities
As of October 19, 2026

	Percent Complete					
Construction Phase	**Hartsville CS & Solar Array**	**Spread 1**	**Spread 2**	**Columbia Gulf M&R**	**Kingston Meter**	**Midwestern and TETLP M&R**
Overall Construction	99%	96%	92%	88%	94%	99%
Mobilization	100%	100%	100%	100%	100%	100%
Site Preparation	99%	100%	100%	100%	100%	100%
Construction Activities	99%	96%	95%	88%	95%	99%
Cleanup	74%	63%	71%	40%	50%	88%
Rough Grading	N/A	64%	78%	85%	100%	100%
Final Grading	N/A	62%	64%	75%	100%	100%
Seeding	N/A	62%	64%	N/A	N/A	N/A
Mulching	N/A	62%	64%	N/A	N/A	N/A
Restoration	74%	62%	74%	40%	50%	99%
Demobilization	74%	30%	30%	75%	75%	85%

ATTACHMENT B

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 09/24/2026
Location: MP 0.1
Direction: East
Description: Right of way permanently vegetated (pasture land)



Date: 09/24/2026
Location: MP 0.3
Direction: East
Description: Right of way permanently vegetated (residential)



Date: 09/24/2026
Location: MP 0.4
Direction: East
Description: Right of way permanently vegetated (residential)



Date: 5/20/2026
Location: MP 0.4
Direction: West
Description: Restoration of residential area in progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 6/29/2026
Location: MP 1.6
Direction: West
Description: Revegetation of pasture in progress



Date: 6/29/2026
Location: MP 2.2
Direction: East
Description: Slope revegetation in progress



Date: 10/08/2026
Location: Hartsville Compressor Station (MP 4.0)
Direction: South
Description: Mainly permanent vegetation



Date: 10/08/2026
Location: Hartsville Compressor Station (MP 4.0)
Direction: Southwest
Description: Permanent vegetation

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/08/2026
Location: Hartsville Compressor Station (MP 4.0)
Direction: Northeast
Description: Permanent vegetation



Date: 9/5/2026
Location: MP 4.9
Direction: East
Description: Steep slope revegetation in progress



Date: 09/24/2026
Location: MP 5.0
Direction: East
Description: Temporary vegetation (steep slope**)**



Date: 9/25/2026
Location: MP 5.1
Direction: West
Description: Permanent vegetation slowly growing (residential)

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 7/31/2026
Location: MP 5.2
Direction: West
Description: Final grade of pasture in progress (slide slope)



Date: 5/16/2026
Location: MP 5.6
Direction: West
Description: Stabilized pasture



Date: 9/18/2026
Location: MP 5.76
Direction: West
Description: Vegetative coverage improving prior to army worms



Date: 9/23/2026
Location: MP 5.76
Direction: West
Description: Impacts from army worms

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 9/24/2026
Location: MP 5.89
Direction: East
Description: Right of way permanently vegetated (pasture land)



Date: 6/3/2026
Location: MP 6.1
Direction: West
Description: Revegetation of pasture in progress



Date: 9/24/2026
Location: MP 7.59
Direction: West
Description: Mix of temporary and permanent vegetation (Hayfield)



Date: 9/24/2026
Location: MP 7.89
Direction: East
Description: Mainly temporary vegetation with some permanent, ECDs remain in place (Steep Slope)

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/7/2026
Location: MP 9.7
Direction: West
Description: Revegetation progress



Date: 09/25/2026
Location: MP 10.0
Direction: East
Description: Mainly temporary vegetation (side slope)



Date: 09/25/2026
Location: MP 10.27
Direction: East
Description: Mainly temporary vegetation (Steep slope)



Date: 7/10/2026
Location: MP 12.9
Direction: Facing East
Description: SS-SMI-T01-001; revegetation in progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 9/25/2026
Location: MP 13.6
Direction: East
Description: Mainly permanent vegetation, landowner cut hay (hay field)



Date: 9/26/2026
Location: MP 13.7
Direction: West
Description: Temporary and permanent vegetation (pasture land)



Date: 8/1/2026
Location: MP 15.4
Direction: Facing West
Description: Steep slope revegetation in progress



Date: 10/12/2026
Location: MP 16.0
Direction: East
Description: Revegetation in progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/14/2026
Location: MP 16.5
Direction: Northeast
Description: Stable, sparsely vegetated forested area



Date: 10/14/2026
Location: MP 17.4
Direction: East
Description: Mainly temporary vegetation in wooded area



Date: 8/28/2026
Location: MP 17.8
Direction: East
Description: Sod installed in residential area



Date: 10/14/2026
Location: MP 18.4
Direction: Northeast
Description: Stable side slope with temporary vegetation

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/7/2026
Location: MP 21.5
Direction: East
Description: Vegetation is limited will be reseeded



Date: 10/7/2026
Location: MP 22.9
Direction: East
Description: Side-slope mix of temporary and permanent vegetation



Date: 10/13/2026
Location: MP 25.8
Direction: West
Description: Sparse vegetation and may need additional seeding



Date: 10/14/2026
Location: MP 29.8
Direction: East
Description: Army worms observed on site and no vegetation

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 9/9/2026
Location: MP 29.8
Direction: East
Description: WW_JAC-T06-005; revegetation in progress



Date: 10/14/2026
Location: MP 30.6
Direction: East
Description: Army worm damage to ROW



Date: 9/11/2026
Location: MP 31.0
Direction: West
Description: Stabilized pasture; revegetation in progress



Date: 10/2/2026
Location: MP 32.8
Direction: West
Description: Slope stabilized; revegetation in progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/7/2026
Location: MP 34.1
Direction: West
Description: Topsoil replacement in progress



Date: 10/9/2026
Location: MP 35.4
Direction: West
Description: Subgrade work in progress



Date: 10/8/2026
Location: MP 38.1
Direction: East
Description: Restoration progress



Date: 10/10/2026
Location: MP 39.8
Direction: West
Description: Restoration progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/3/2026
Location: MP 43.7
Direction: East
Description: SS-JAC-T08-018 revegetation progress



Date: 10/3/2026
Location: MP 44.6
Direction: East
Description: SS-JAC-T07-013 revegetation progress



Date: 10/9/2026
Location: MP 48.1
Direction: East
Description: Revegetation progress at SS-PUT-T05-055



Date: 10/8/2026
Location: MP 48.7
Direction: East
Description: Excavator pulling mats to initiate subgrade and restoration work

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/1/2026
Location: MP 50.9
Direction: East
Description: Steep slope revegetated; revegetation in progress at SS-PUT-T10-003



Date: 10/2/2026
Location: MP 53.3
Direction: Northwest
Description: Backfilling after a dig up and repair operation



Date: 10/6/2026
Location: MP 56.6
Direction: East
Description: Rough grading in progress




Date: 10/10/2026
Location: MP 60.1
Direction: East
Description: Rough grading progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 60.0
Direction: East
Description: Pending cleanup

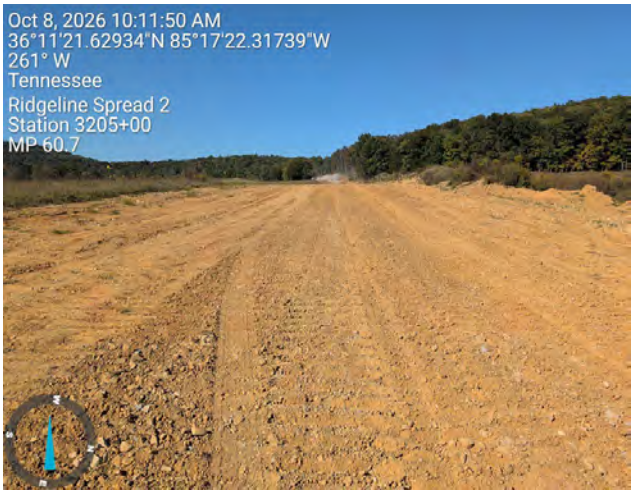

Date: 10/8/2026
Location: MP 61.0
Direction: West
Description: Pending cleanup



Date: 10/8/2026
Location: MP 61.3
Direction: West
Description: Pending cleanup



Date: 10/8/2026
Location: MP 61.9
Direction: Northwest
Description: Pending cleanup


East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 62.2
Direction: Northwest
Description: Pending cleanup



Date: 10/8/2026
Location: MP 63.4
Direction: Northwest
Description: Pending cleanup

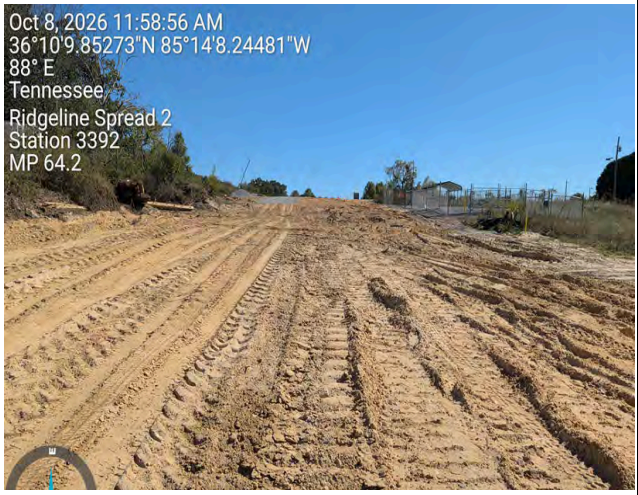

Date: 10/8/2026
Location: MP 64.2
Direction: East
Description: Pending cleanup




Date: 10/8/2026
Location: MP 65.2
Direction: Northwest
Description: Pending cleanup

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 66.0
Direction: West
Description: Pending cleanup

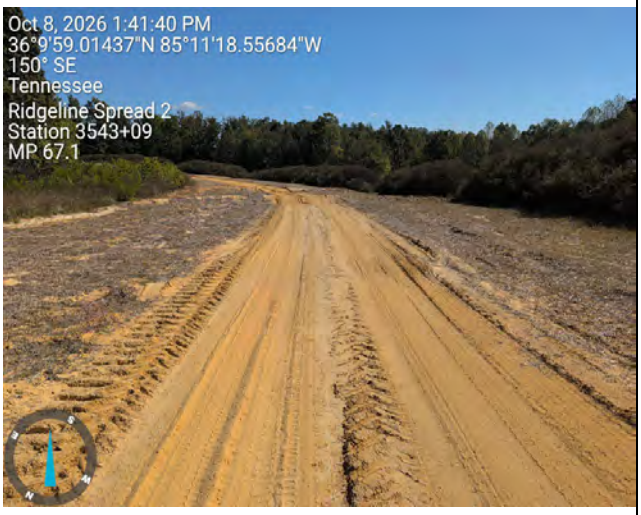

Date: 10/8/2026
Location: MP 67.1
Direction: Southeast
Description: Pending cleanup



Date: 10/8/2026
Location: MP 68.2
Direction: East
Description: Cleanup underway



Date: 10/8/2026
Location: MP 68.4
Direction: East
Description: Cleanup underway Obey River

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 69.0
Direction: East
Description: Restored slope



Date: 10/8/2026
Location: MP 69.6
Direction: West
Description: Recently restored ROW



Date: 10/8/2026
Location: MP 69.6
Direction: East
Description: Recently restored ROW



Date: 10/8/2026
Location: MP 70.7
Direction: West
Description: Temporary cover crop

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log

<table>
<tr>
<td>
</td>
<td>
</td>
</tr>
<tr>
<td>Date: 10/8/2026
Location: MP 71.5
Direction: East
Description: Recently restored ROW</td>
<td>Date: 10/8/2026
Location: MP 71.5
Direction: East
Description: Restored Little Hurricane Creek</td>
</tr>
<tr>
<td>
</td>
<td>
</td>
</tr>
<tr>
<td>Date: 10/8/2026
Location: MP 72.6
Direction: East
Description: Recently restored ROW</td>
<td>Date: 10/8/2026
Location: MP 73.3
Direction: East
Description: Recently restored ROW</td>
</tr>
</table>

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 74.1
Direction: East
Description: Restoration underway



Date: 9/09/2026
Location: MP 75.1
Direction: Northeast
Description: Good cover crop coverage



Date: 9/8/2026
Location: MP 75.9
Direction: Southwest
Description: Stable ROW with cover crop



Date: 9/8/2026
Location: MP 76.7
Direction: East
Description: Reseeding needed


East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 80.5
Direction: East
Description: Clarkrange Station



Date: 8/21/2026
Location: MP 82.8
Direction: Southwest
Description: Fence restoration

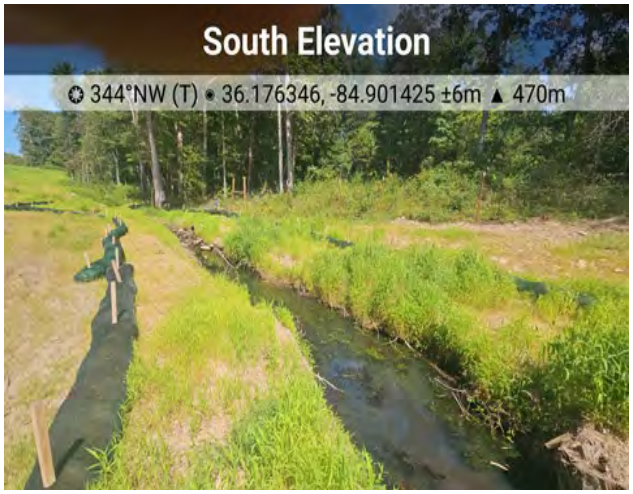

Date: 8/27/2026
Location: MP 83.7
Direction: Northwest
Description: Stream bank growth



Date: 8/28/2026
Location: MP 84.5
Direction: East
Description: Pond restoration complete with pond filling up

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log




Date: 8/17/2026
Location: MP 85.8
Direction: Northeast
Description: Bare spots need reseeding



Date: 8/11/2026
Location: MP 87.1
Direction: East
Description: Minor permanent grass growth, reseeding will be needed



Date: 10/2/2026
Location: MP 88.08
Direction: Southeast
Description: Landowner disturbance from private gas line install

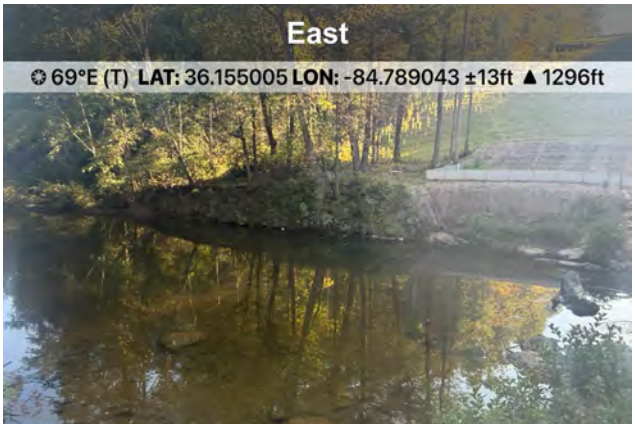

Date: 10/8/2026
Location: MP 89.6
Direction: East
Description: Whites Creek post restoration

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log

<table>
<tr>
<td>
</td>
<td>
</td>
</tr>
<tr>
<td>Date: 10/8/2026
Location: MP 90.9
Direction: East
Description: Test site restored</td>
<td>Date: 10/8/2026
Location: MP 90.9
Direction: Northeast
Description: Testing site lake tanks to be removed</td>
</tr>
<tr>
<td>
</td>
<td>
</td>
</tr>
<tr>
<td>Date: 10/8/2026
Location: MP 92.3
Direction: East
Description: Restored ROW, punch list crew has reseeded</td>
<td>Date: 10/8/2026
Location: MP 92.8
Direction: West
Description: Restored ROW</td>
</tr>
</table>

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 93.2
Direction: West
Description: Dig site restored



Date: 10/8/2026
Location: MP 93.2
Direction: East
Description: MLV site, pending cleanup



Date: 10/8/2026
Location: MP 93.3
Direction: Southwest
Description: Gordons Branch, stabilized slopes and buffers



Date: 10/8/2026
Location: MP 93.4
Direction: West
Description: Restored ROW (residential)

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 93.4
Direction: Southwest
Description: Restored ROW (view to MLV site above Gordons Branch)



Date: 10/8/2026
Location: MP 94.0
Direction: South
Description: Restored ROW (Residential)



Date: 10/8/2026
Location: MP 94.4
Direction: Southeast
Description: Restored ROW (Little Clear Creek)



Date: 10/8/2026
Location: MP 95.0
Direction: West
Description: Restored ROW

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 95.8
Direction: Southwest
Description: Restored ROW



Date: 10/8/2026
Location: MP 95.9
Direction: West
Description: Restored ROW (residential area reseeded by punch list crew)



Date: 10/8/2026
Location: MP 97.8
Direction: Northeast
Description: Restored ROW (controls removed)



Date: 10/8/2026
Location: MP 98.6
Direction: East
Description: ROW reworked and stabilized

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log




Date: 10/8/2026
Location: MP 98.6
Direction: East
Description: ROW reworked and stabilized



Date: 10/8/2026
Location: MP 99.4
Direction: Southwest
Description: Recently restored ROW



Date: 10/8/2026
Location: MP 99.4
Direction: East
Description: Recently restored ROW

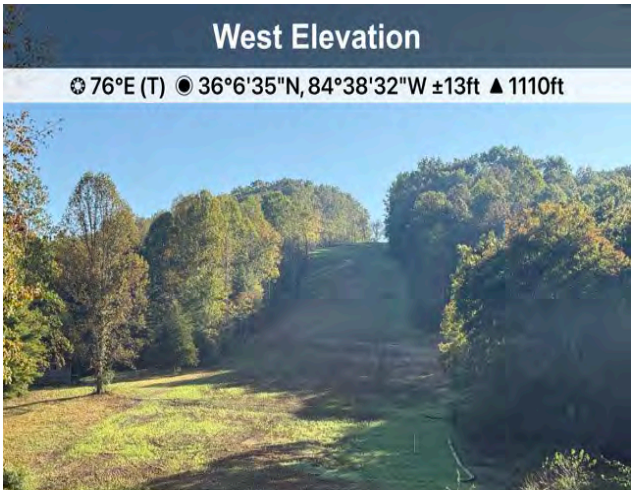

Date: 10/8/2026
Location: MP 100.3
Direction: West
Description: Restored ROW

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 101.4
Direction: West
Description: Cleanup underway in residential area



Date: 10/8/2026
Location: MP 101.7
Direction: Northwest
Description: Cleanup underway in residential area




Date: 10/8/2026
Location: MP 102.2
Direction: North
Description: Hydro mulching in progress



Date: 10/8/2026
Location: MP 102.8
Direction: Southwest
Description: Cleanup in progress

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log

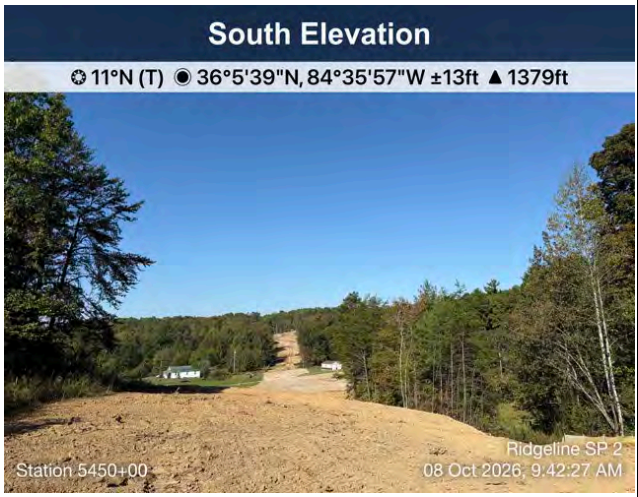

Date: 10/8/2026
Location: MP 103.2
Direction: South
Description: Cleanup in progress



Date: 10/8/2026
Location: MP 104.7
Direction: Northwest
Description: Cleanup in progress





Date: 10/8/2026
Location: MP 105.6
Direction: Southwest
Description: Cleanup in progress




Date: 10/8/2026
Location: MP 106.5
Direction: Southeast
Description: Restored ROW

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log
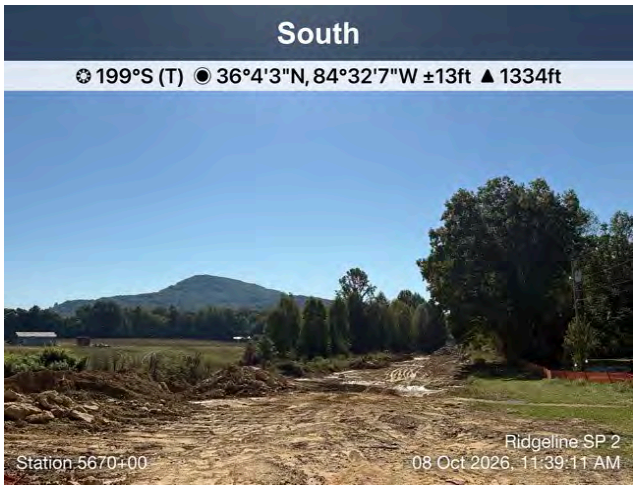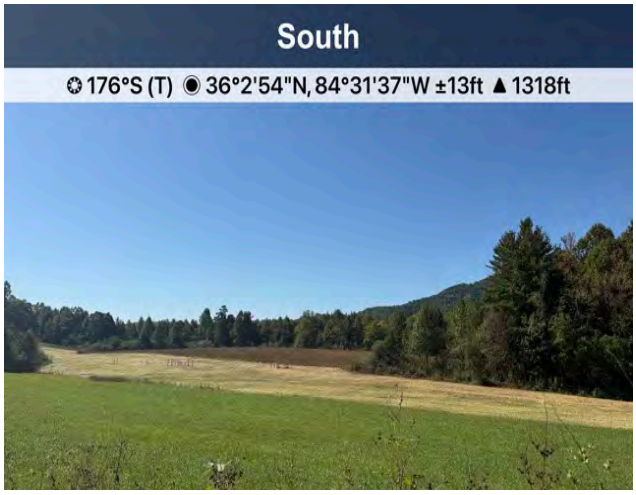
<table>
<tr>
<td>
</td>
<td>
</td>
</tr>
<tr>
<td>Date: 10/8/2026
Location: MP 107.4
Direction: South
Description: Pending cleanup</td>
<td>Date: 10/8/2026
Location: MP. 108.0
Direction: South
Description: Pending cleanup</td>
</tr>
<tr>
<td>
</td>
<td>
</td>
</tr>
<tr>
<td>Date: 10/8/2026
Location: MP 108.9
Direction: South
Description: Recently restored ROW</td>
<td>Date: 10/8/2026
Location: MP 109.5
Direction: Northwest
Description: Restored ROW</td>
</tr>
</table>

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log

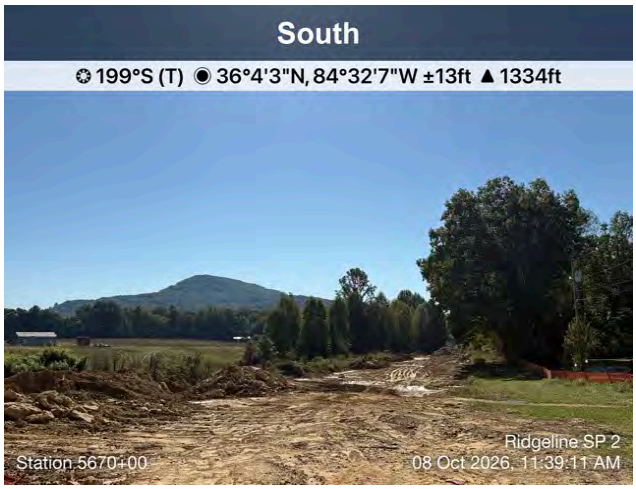

Date: 10/8/2026
Location: MP 107.4
Direction: South
Description: Pending cleanup



Date: 10/8/2026
Location: MP 108.0
Direction: South
Description: Pending cleanup



Date: 10/8/2026
Location: MP 108.9
Direction: South
Description: Recently restored ROW




Date: 10/8/2026
Location: MP 109.5
Direction: Northwest
Description: Restored ROW


East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 110.3
Direction: West
Description: Recently Restored ROW

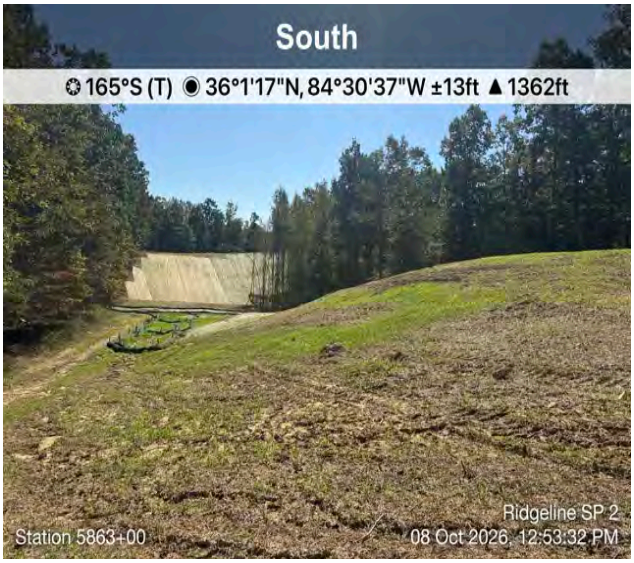

Date: 10/8/2026
Location: MP 111.0
Direction: South
Description: Recently restored ROW

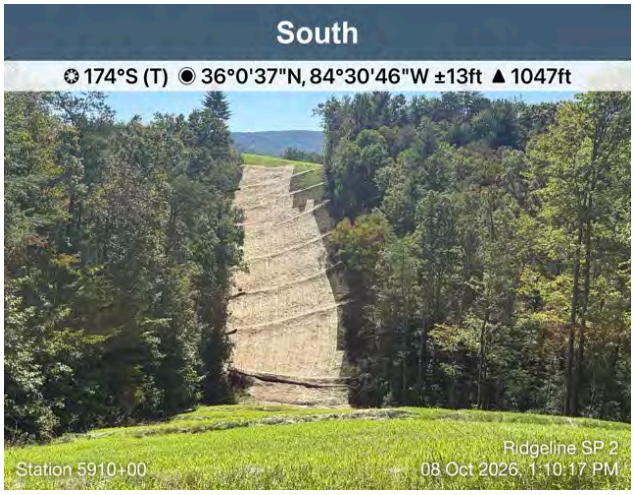


Date: 10/8/2026
Location: MP 111.9
Direction: South
Description: Recently restored ROW



Date: 10/8/2026
Location: MP 112.2
Direction: North
Description: Restored ROW pending cleanup

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log

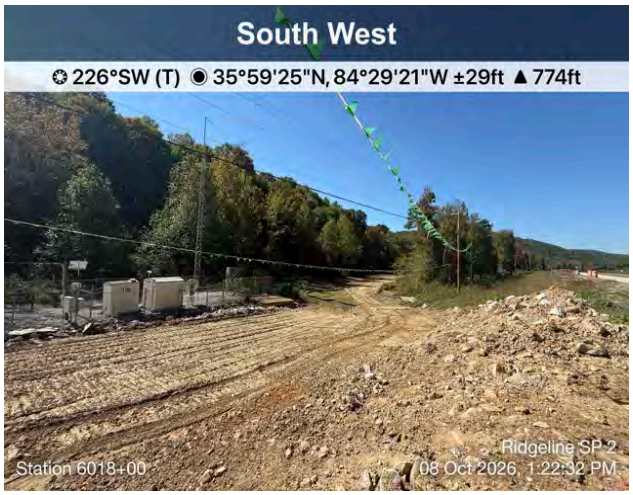

Date: 10/8/2026
Location: MP 113.9
Direction: Southwest
Description: Pending Cleanup



Date: 10/8/2026
Location: MP 114.2
Direction: Southwest
Description: Harriman Station



Date: 10/8/2026
Location: MP 114.4
Direction: Southwest
Description: Recently restored ROW



Date: 10/8/2026
Location: MP 115.9
Direction: Southwest
Description: Pending cleanup


East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 116.45
Direction: Northwest
Description: Restored ROW (Emory Backwater)



Date: 10/8/2026
Location: MP 117.10
Direction: Northeast
Description: Pending Cleanup

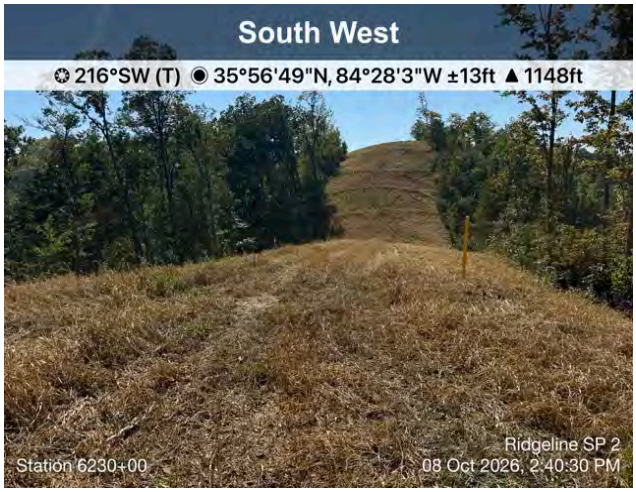

Date: 10/8/2026
Location: MP 118.0
Direction: Southwest
Description: Restored ROW



Date: 10/8/2026
Location: MP 119.3
Direction: Northwest
Description: Restored ROW


East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001
Photo Log



Date: 10/8/2026
Location: MP 119.4
Direction: South
Description: Restored ROW (Kings Creek)



Date: 10/8/2026
Location: MP 120.1
Direction: Southwest
Description: Restored ROW

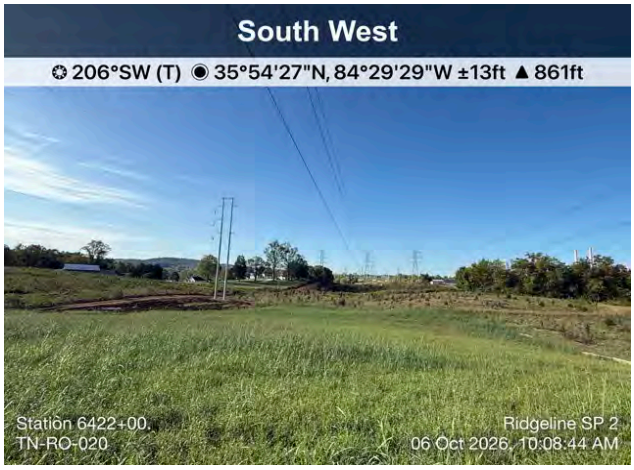

Date: 10/8/2026
Location: MP 121.6
Direction: Southwest
Description: Restored ROW



Date: 10/8/2026
Location: MP 122.31
Direction: North
Description: TVA termination

ATTACHMENT C

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Docket Nos. CP23-516-000 and CP23-516-001

Restoration and Post-Construction Monitoring Plan

October 2026

Table of Contents

ACRONYMS / ABBREVIATIONS 4
1.0 Introduction and Current Status 5
2.0 Right-of-Way Restoration Status and Schedule 6
3.0 Waterbody and Wetland Monitoring and Restoration Framework 7
4.0 Water Quality Testing 8
5.0 Cultural Artifact Delivery 8

TABLES
Table 1-1: Project Restoration Activities Estimated Percent Complete by Quarter 5

ATTACHMENTS 9
Attachment A - Restoration Table 10

ACRONYMS / ABBREVIATIONS

ARAP	Aquatic Resource Alteration Permit
Commission	Federal Energy Regulatory Commission
FEIS	Final Environmental Impact Statement
FERC	Federal Energy Regulatory Commission
FERC Plan	Upland Erosion Control, Revegetation and Maintenance Plan (March 2013)
FERC Procedures	Wetland and Waterbody Construction and Mitigation Procedures (March 2013)
Guidance Document	Water Well and Spring Testing Program Guidance Document
MP	Milepost
NOT	Notice of Termination
NPDES	National Pollutant Discharge Elimination System
NRCS	Natural Resources Conservation Service
Plan	Restoration and Post-Construction Monitoring Plan
Project	Ridgeline Project
TDEC	Tennessee Department of Environment and Conservation
ETNG	East Tennessee Natural Gas, L.L.C.
USACE	United States Army Corps of Engineers

1.0 Introduction and Current Status

East Tennessee Natural Gas, LLC ("ETNG") is providing this Restoration and Post-Construction Monitoring Plan ("Plan") to inform the Federal Energy Regulatory Commission ("Commission" or "FERC") and other stakeholders of the scope and anticipated schedule for final restoration activities associated with the Ridgeline Expansion Project ("Project"), as well as to summarize remaining post-construction monitoring requirements under approved permits.

Construction activities for the Project began in October 2025. As of the date of this Plan, approximately 64 percent of the Project area has been restored, representing an estimated 78.2-miles of the total 122.2-mile Project length. Restoration activities will continue as construction activities are completed, with full initial restoration anticipated by December 1, 2026. Additional restoration and revegetation will occur in Spring 2027, with full restoration completion expected by the end of June 2027, as summarized in **Table 1-1**. Post-construction monitoring surveys of the project area and resources will be completed in summer 2027.

Table 1-1: Ridgeline Expansion Project Restoration Activities Estimated Percent Complete

Time Period	Spread 1	Spread 2	Actual or Estimated Percent Complete
Current	60%	68%	64%
Nov-Dec 2026	70-90%	70-90%	70-90%
Jan-Mar 2027	100%	100%	100%
Apr-Jun 2027*	100%	100%	100%

*Project will be considered "fully restored" apart from areas needing additional work, maintenance, restoration, etc.

Final restoration of the Project area, which includes grading, topsoil replacement, seeding, and mulching, will be completed in accordance with the requirements of applicable Project documents, including the Final Environmental Impact Statement issued by the FERC, FERC's Upland Erosion Control, Revegetation and Maintenance Plan ("FERC Plan"), FERC's Wetland and Waterbody Construction and Mitigation Procedures ("FERC Procedures"), and applicable federal and state regulations.

As part of final restoration for the Project, ETNG will inspect areas that were previously restored to monitor post-construction restoration success. Consistent with the FERC Plan, restoration will be considered successful when the right-of-way surface condition is comparable to adjacent undisturbed lands, construction debris has been removed (unless otherwise approved by the landowner or land-managing agency), revegetation is successful, and proper drainage has been restored. Revegetation will be considered successful when visual inspections confirm that the density and cover of non-nuisance vegetation are comparable to those of adjacent undisturbed areas. In addition, ETNG will ensure that current and future areas of subsidence that have occurred in the Project area are addressed in accordance with the plan and a schedule will be provided with ETNG's Project status reports to the Commission.

ETNG has been and is committed to environmental protection and transparent communication with stakeholders throughout Project construction and restoration activities. Project restoration updates will continue to be included in compliance reports, and the Commission and other stakeholders will be notified of any changes to projected schedules. Following completion of final restoration, ETNG will monitor the right-of-way for at least three years in accordance with the Commission and other

federal and state requirements to verify site stability and successful revegetation or until all applicable agency restoration requirements have been met.

2.0 Right-of-Way Restoration Status and Schedule

Attachment A summarizes pipeline restoration progress by milepost ("MP") and presents the anticipated schedule for achieving final restoration and stabilization. Ground disturbance activities are expected to end by December 1, 2026, barring unforeseen restoration-related issues. Final stabilization includes the establishment of permanent vegetation, placement of permanent non-eroding surfaces, or the resumption of normal agricultural practices.

Areas that have not achieved final stabilization will continue to be monitored until appropriate conditions are achieved. Following final restoration, status reports will be submitted to the Commission and will identify any problem areas or landowner concerns. The anticipated restoration timeframes presented in **Attachment A** are subject to weather conditions and other external factors. ETNG expects to employ a post-construction workforce of approximately 37 personnel in three crews and adequate equipment over the Project area that will be focused on restoration.

Project restoration will utilize seed mixes composed of native species or otherwise approved by the applicable agencies. Unless requested by a landowner or land-managing agency, as described in the Project Storm Water Pollution Prevention Plan ("SWPPP") and the Project's Final Environmental Impact Statement ("FEIS"), Natural Resources Conservation Service ("NRCS") approved seed mixes and in a manner that maximizes benefits to pollinators. ETNG personnel will routinely inspect the right-of-way to monitor revegetation in accordance with applicable requirements. During post-construction restoration, ETNG will maintain travel lanes and temporary access roads as needed to ensure safe, environmentally protective access to Project sites and to minimize impacts to local residents. In accordance with the FERC Plan, ETNG will conduct topsoil and subsoil compaction testing in disturbed agricultural and residential areas and implement appropriate mitigation measures. ETNG will also monitor and address drainage and irrigation issues in agricultural areas until restoration is deemed successful and will comply with all post-construction vegetation mowing and clearing requirements.

3.0 Waterbody and Wetland Monitoring and Restoration Framework

Monitoring of restoration activities for stream and wetlands are outlined in authorizations received from the Commission, the United States Army Corps of Engineers ("USACE"), and TDEC. ETNG intends to conduct post construction monitoring for a minimum of three (3) years in accordance with all agency requirements. ETNG will prepare a single annual monitoring report suitable for submission to all agencies.

Sections V.C., V.D., VI.C. and D. of the FERC Procedures outline restoration, post-construction maintenance, and reporting requirements for FERC regulated waterbodies and wetlands. As described in Section VI.D.4 of the FERC Procedures, monitoring must occur annually to assess wetland revegetation until wetland revegetation is successful. Section VI.D.6 of the FERC Procedures requires a report to be filed with the Commission within three years after construction, identifying the status of the revegetation efforts and documenting success or providing a remedial revegetation plan to actively revegetate wetlands. Thereafter, annual reports are required until wetland revegetation is successful.

The permit conditions and special conditions of the Project's USACE Permit (LRN-2021-00844) do not directly require post-construction restoration monitoring, although Permit Condition 5 and Special Condition 6 reference the Aquatic Resource Alteration Permit ("ARAP") (NRS 24.014) issued by TDEC, which also serves as the Project's Section 401 Water Quality Certification. The USACE permit requires ETNG to follow all conditions of the ARAP. ETNG will therefore provide the USACE a copy of the annual monitoring report required by the ARAP.

Part I, Authorized Work Special Condition f. of the ARAP requires an annual post-construction monitoring report to TDEC for three years following the Project's completion. Monitoring requirements are outlined in Part II, Monitoring Requirements Part b. of the ARAP:

> b. An annual post-construction monitoring report must be submitted by April 30 each year for three years after the project's completion (per Special Condition f above) to document evidence of the maintenance of jurisdictional status and successful restoration within **all impacted jurisdictional features**, and shall include:
> 1. Representative photographs of each feature pre-impact and post-impact
> 2. Wetland delineations and stream hydrologic determinations. All stream hydrologic determinations must be made during the February 1 – April 15 time period each year and in accordance with the procedures in TDEC Rule 0400-40-03-.05(9)
> 3. Identification of any features that have not returned to pre-impact condition, and a corresponding proposed adaptive management plan

Stream hydrologic determinations specified under Part II.b.2. of the ARAP for this Project are limited to perennial and intermittent waterbodies that were also determined to be TDEC jurisdictional Streams following a pre-construction hydrologic determination. Waterbodies that were determined by TDEC to be wet weather conveyances (or ephemeral streams for this Project) will not require a stream hydrologic determination.

4.0 Water Quality Testing

ETNG offered pre-construction water sampling for all public and private ground water supply wells and potable springs (Water Sources) within 300 feet of the Project's pipeline construction areas ETNG received landowner permission to conduct pre-construction sampling 31 locations.

ETNG will contact landowners where pre-construction sampling was conducted for permission to conduct post-construction sampling.

If the water quality of a well is determined to have been impaired by Project construction, ETNG will provide a temporary source of drinking water for the landowner/well user within five (5) business days of the determination of impairment. Any Water Source whose water quality or yield is determined to have been impaired by the construction of the Project (including blasting) will be re-tested within thirty (30) calendar days of the determination of impairment. If supplemental testing and evaluation still shows impaired yield or water quality as a result of Project construction, ETNG promptly will arrange for a permanent resolution of the impairment by providing the landowner: (a) a treatment system, new well, reconstruction of a spring, or another source of water of a quality and yield equal to or better than the water supplied by the Water Source prior to the construction of the Project, as soon as and to the extent reasonably practicable, or (b) reasonable monetary compensation.

5.0 Cultural Artifact Delivery

ETNG will continue to complete and deliver data recovery reports as they are prepared, with the final reports being submitted to FERC no later than February 11, 2027. Additionally, artifacts will be returned to landowners beginning in December 2026. Returned artifacts will be cataloged and the receipt by landowners documented via a signed returned artifact acknowledgement form.

ATTACHMENTS

Attachment A - Restoration Table

RIDGELINE EXPANSION PROJECT RESTORATION TABLE

Updated as of October 13, 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	0+00	1+66	0	0.03	Complete	Restored	Upland	May 2026
1	1+66	20+83	0.03	0.39	Complete	Restored	Upland	May 2026
1	15+70	15+70	0.30	0.30	Complete	Restored	Intermittent	May 2026
1	20+83	21+15	0.39	0.04	Complete	Restored	Upland	May 2026
1	25+35	25+83	0.48	0.49	Complete	Restored	Perennial	May 2026
1	24+15	25+63	0.46	0.49	Complete	Restored	Upland	May 2026
1	25+63	33+72	0.49	0.64	Complete	Restored	Upland	May 2026
1	33+72	35+72	0.64	0.68	Complete	Restored	Upland	May 2026
1	42+33	44+95	0.8	0.85	Complete	Restored	Upland	May 2026
1	55+87	56+32	1.06	1.07	Complete	Restored	Upland	May 2026
1	56+32	65+80	1.07	1.25	Complete	Restored	Upland	May 2026
1	65+80	72+20	1.25	1.37	Complete	Restored	Upland	May 2026
1	72+10	72+16	1.37	1.37	Complete	Restored	Perennial	May 2026
1	72+20	78+97	1.37	1.5	Complete	Restored	Upland	May 2026
1	78+97	81+67	1.5	1.55	Complete	Restored	Upland	May 2026
1	84+34	86+91	1.6	1.65	Complete	Restored	Upland	May 2026
1	92+83	100+28	1.76	1.9	Complete	Restored	Upland	May 2026
1	101+52	101+64	1.92	1.93	Complete	Restored	Intermittent	June 2026
1	104+65	104+75	1.98	1.98	Complete	Restored	Ephemeral	June 2026
1	110+89	114+57	2.10	2.17	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	114+44	114+65	2.17	2.17	Complete	Restored	Intermittent	June 2026
1	118+44 137+31	120+17 138+49	2.24 2.60	2.28 2.62	Complete	Restored	Upland	June 2026
1	123+91	123+91	2.35	2.35	Complete	Restored	Ephemeral	June 2026
1	130+33	130+33	2.47	2.47	Complete	Restored	Intermittent	June 2026
1	139+26	145+29	2.64	2.75	Complete	Restored	Upland	June 2026
1	142+43	143+55	2.70	2.72	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	143+62	145+86	2.72	2.84	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	146+26	148+15	2.77	2.81	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	148+15	136+11	2.81	2.58	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	164+56	170+70	3.12	3.23	Complete	Restored	Upland	September 2026
1	172+52	175+76	3.27	3.33	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	177+31	177+31	3.35	3.35	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	177+40	177+63	3.35	3.36	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	179+52	179+52	3.40	3.40	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	190+08	190+08	3.60	3.60	Complete	Restored	Ephemeral	July 2026
1	216+48	21648.00	4.09	4.10	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	256+89	257+93	4.87	4.89	Complete	Restored	Upland	June 2026
1	257+93	259+90	4.89	4.92	Complete	Restored	Upland	June 2026
1	259+90	269+78	4.92	5.11	Complete	Restored	Upland	June 2026
1	263+17	263+27	4.98	4.99	Complete	Restored	Intermittent	June 2026
1	263+28	263+28	4.99	4.99	Complete	Restored	Ephemeral	June 2026
1	270+52	275+29	5.12	5.21	Complete	Restored	Upland	June 2026
1	275+29	296+05	5.21	5.61	Complete	Restored	Upland	June 2026
1	296+48	303+67	5.62	5.75	Complete	Restored	Upland	June 2026
1	304+02	305+68	5.76	5.79	Complete	Restored	Upland	June 2026
1	306+17	319+19	5.8	6.05	Complete	Restored	Upland	June 2026
1	311+52	319+64	**5.90**	6.05	Complete	Restored	Intermittent	May 2026
1	316+80	316+80	**6.00**	6.00	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	333+70	346+36	6.32	6.56	Complete	Restored	Upland	September 2026
1	345+57	369+60	6.54	7.00	Complete	Restored	Upland	September 2026
1	369+60	369+60	**7.00**	7.00	Complete	Restored	Upland	September 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	381+88	381+88	7.23	7.23	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	385+87	409+06	7.31	7.75	Complete	Restored	Upland	June 2026
1	412+40	412+40	7.81	7.81	Complete	Restored	Ephemeral	June 2026
1	413+33	417+28	7.83	7.9	Complete	Restored	Upland	June 2026
1	417+41	417+46	7.91	7.91	Complete	Restored	Perennial	June 2026
1	420+39	420+57	7.96	7.97	Complete	Restored	Perennial	June 2026
1	440+84	440+84	8.35	8.35	Complete	Restored	Ephemeral	June 2026
1	464+64	464+64	8.80	8.80	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	473+99	473+99	8.98	8.98	Complete	Restored	Ephemeral	June 2026
1	480+48	480+48	9.10	9.10	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	485+42	485+70	9.19	9.20	Complete	Restored	Perennial	June 2026
1	497+72	579+50	9.43	10.98	Complete	Restored	Upland	June 2026
1	512+35	512+42	9.70	9.70	Complete	Restored	Perennial	June 2026
1	513+44	513+51	9.72	9.73	Complete	Restored	Perennial	June 2026
1	514+00	515+00	9.73	9.75	Complete	Restored	Upland	June 2026
1	549+12	549+12	10.40	10.40	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	580+22	583+88	10.99	11.06	Complete	Restored	Upland	September 2026
1	585+00	591+85	11.08	11.21	Complete	Restored	Upland	June 2026
1	596+33	596+61	11.29	11.30	Complete	Restored	Perennial	June 2026
1	603+47	603+65	11.43	11.43	Complete	Restored	Perennial	June 2026
1	603+63	622+25	11.43	11.79	Complete	Restored	Upland	June 2026
1	628+83	628+87	11.91	11.91	Complete	Restored	Perennial	June 2026
1	647+87	647+87	12.27	12.27	Complete	Restored	Intermittent	June 2026
1	652+72	677+47	12.36	12.83	Complete	Restored	Upland	June 2026
1	683+13	683+65	12.94	12.95	Complete	Restored	Perennial	June 2026
1	703+85	703+90	13.33	13.33	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	718+08	718+08	13.60	13.60	Complete	Restored	Ephemeral	June 2026
1	725+52	731+23	13.74	13.85	Complete	Restored	Upland	June 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	731+65	731+65	13.86	13.86	Complete	Restored	Ephemeral	June 2026
1	733+92	733+92	13.90	13.90	Complete	Restored	Ephemeral	June 2026
1	745+61	745+61	14.12	14.12	Complete	Restored	Intermittent	June 2026
1	770+89	770+89	14.60	14.60	Complete	Restored	Intermittent	July 2026
1	777+66	777+66	14.73	14.73	Complete	Restored	Intermittent	July 2026
1	782+54	782+61	14.82	14.82	Complete	Restored	Ephemeral	July 2026
1	787+96	788+06	14.92	14.93	Complete	Restored	Perennial	July 2026
1	792+00	792+00	15.00	15.00	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	795+16	799+65	15.06	15.14	Complete	Restored	Upland	July 2026
1	801+73	813+15	15.18	15.4	Complete	Restored	Upland	July 2026
1	822+48	842+57	15.58	15.96	Complete	Restored	Upland	July 2026
1	847+85	847+89	16.06	16.06	Complete	Restored	Perennial	July 2026
1	857+68	857+68	16.24	16.24	Complete	Restored	Intermittent	July 2026
1	864+45	864+45	16.37	16.37	Complete	Restored	Intermittent	July 2026
1	873+09	873+09	16.54	16.54	Complete	Restored	Ephemeral	August 2026
1	876+83	876+83	16.61	16.61	Complete	Restored	Intermittent	August 2026
1	878+90	878+98	16.65	16.65	Complete	Restored	Perennial	August 2026
1	894+83	894+83	16.95	16.95	Complete	Restored	Intermittent	August 2026
1	909+52	909+67	17.23	17.23	Complete	Restored	Perennial	August 2026
1	914+73	91532.00	17.32	17.34	Complete	Restored	Perennial	August 2026
1	920+92	921+07	17.44	17.44	Complete	Restored	Perennial	August 2026
1	925+33	925+37	17.53	17.53	Complete	Restored	Perennial	August 2026
1	938+88	938+88	17.78	17.78	Complete	Restored	Ephemeral	August 2026
1	947+05	947+05	17.94	17.94	Complete	Restored	Ephemeral	August 2026
1	947+53	947+53	17.95	17.95	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	967+89	985+73	18.33	18.67	Complete	Restored	Upland	July 2026
1	974+06	974+59	18.45	18.46	Complete	Restored	Perennial	July 2026
1	985+73	1008+25	18.67	19.1	Complete	Restored	Upland	July 2026
1	1004+50	1004+50	19.0	19.0	Complete	Restored	Upland	July 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	1008+25	1041+02	19.1	19.72	Complete	Restored	Upland	July 2026
1	1041+02	1047+11	19.72	19.83	Complete	Restored	Upland	July 2026
1	1041+43	1083+30	19.72	20.52	Complete	Restored	Upland	July 2026
1	1060+40	1070+50	20.08	20.27	Complete	Restored	Upland	July 2026
1	1083+30	1089+19	20.52	20.63	Complete	Restored	Upland	July 2026
1	1089+36	1100+41	20.63	20.84	Complete	Restored	Upland	July 2026
1	1100+41	1114+58	20.84	21.11	Complete	Restored	Upland	July 2026
1	1165+17	1165+23	22.07	22.07	Complete	Restored	Perennial	September 2026
1	1173+50	1173+50	22.23	22.23	Complete	Restored	Intermittent	September 2026
1	1181+47	1181+93	22.38	22.39	Complete	Restored	Intermittent	September 2026
1	1195+10	1195+10	22.63	22.63	Complete	Restored	Ephemeral	August 2026
1	1202+93	1203+00	22.78	22.78	Complete	Restored	Perennial	August 2026
1	1205+62	1206+32	22.83	22.85	Complete	Restored	Perennial	August 2026
1	1217+36	1231+07	23.06	23.32	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1242+85	1242+85	23.54	23.54	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1240+80	1240+80	23.50	23.50	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1248+52	1248+52	23.65	23.65	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1249+22	1249+22	23.66	23.66	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1267+96	1272+60	24.01	24.1	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
1	1278+56	1278+57	24.22	24.24	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1280+29	1280+29	24.25	24.25	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1294+82	1295+14	24.52	24.53	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1317+60	1317+60	24.95	24.95	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1327+06	1348+93	25.13	25.55	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	1342+03	1342+03	25.42	25.42	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1353+69	1353+69	25.64	25.64	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1355+34	1359+78	25.67	25.75	Incomplete	Incomplete	Upland	November 2026
1	1366+91	1366+91	25.89	25.89	Resource restored, ROW incomplete	Restored	Ephemeral	November 2026
1	1370+57	1370+97	25.96	25.97	Incomplete	Incomplete	Upland	November 2026
1	1370+97	1372+58	25.97	26	Incomplete	Incomplete	Upland	November 2026
1	1372+58	1374+45	26	26.03	Incomplete	Incomplete	Upland	November 2026
1	1374+45	1378+62	26.03	26.11	Incomplete	Incomplete	Upland	November 2026
1	1378+62	1388+32	26.11	26.29	Incomplete	Incomplete	Upland	November 2026
1	1388+32	1394+73	26.29	26.42	Incomplete	Incomplete	Upland	November 2026
1	1394+65	1394+86	26.41	26.42	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1406+56	1406+56	26.64	26.64	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1411+57	1411+57	26.73	26.73	Resource restored, ROW incomplete	Restored	Ephemeral	November 2026
1	1431+36	1431+36	27.11	27.11	Resource restored, ROW incomplete	Restored	Ephemeral	November 2026
1	1450+14	1450+14	27.46	27.46	Complete	Restored	Ephemeral	September 2026
1	1456+33	1458+40	27.58	27.62	Incomplete	Incomplete	Upland	November 2026
1	1484+76	1484+89	28.12	28.12	Complete	Restored	Intermittent	September 2026
1	1489+50	1489+50	28.21	28.21	Complete	Restored	Intermittent	September 2026
1	1497+02	1501+07	28.35	28.43	Complete	Restored	Perennial	May 2026
1	1501+07	1503+53	28.43	28.48	Complete	Restored	Perennial	May 2026
1	1505+56	1515+69	28.51	28.71	Complete	Restored	Perennial	May 2026
1	1553+80	1559+66	29.43	29.54	Complete	Restored	Perennial	May 2026
	1566+65	1573+94	29.67	29.81	Incomplete	Incomplete	Upland	November 2026
1	1576+77	1576+77	29.86	29.86	Complete	Restored	Ephemeral	September 2026
1	1587+19	1596+50	30.06	30.24	Incomplete	Incomplete	Upland	November 2026
1	1618+90	1618+90	30.66	30.66	Complete	Restored	Ephemeral	September 2026
1	1610+40	1610+40	30.50	30.50	Complete	Restored	Ephemeral	September 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	1631+52	1631+52	30.90	30.90	Resource restored, ROW incomplete	Incomplete	Pond	November 2026
1	1637+98	1654+69	31.02	31.34	Incomplete	Incomplete	Upland	November 2026
1	1673+18	1673+63	31.69	31.70	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1676+33	1680+33	31.75	31.82	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1682+41	1688+01	31.86	31.97	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1688+03	1696+76	31.97	32.14	Incomplete	Incomplete	Upland	November 2026
1	1697+11	1709+05	32.14	32.37	Incomplete	Incomplete	Upland	November 2026
1	1788+97	1788+97	32.50	33.88	Resource restored, ROW incomplete	Restored	Intermittent	October 2026
1	1789+25	1789+25	33.89	33.89	Resource restored, ROW incomplete	Restored	Ephemeral	October 2026
1	1795+85	1805+92	34.01	34.2	Incomplete	Incomplete	Upland	November 2026
1	1830+64	1830+87	34.67	34.68	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	1833+96	1833+96	34.73	34.73	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1848+22	1848+22	35.00	35.00	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1871+61	1871+61	35.45	35.45	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	1897+62	1898+05	35.94	35.95	Incomplete	Incomplete	Perennial	November 2026
	1897+95	1912+19	35.95	36.22	Incomplete	Incomplete	Upland	November 2026
	1912+19	1924+13	36.22	36.44	Incomplete	Incomplete	Upland	November 2026
1	1923+93	1924+33	36.44	36.45	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1957+03	1957+34	37.06	37.07	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	1986+05	1986+05	37.61	37.61	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2007+94	2008+06	38.03	38.03	Resource restored, ROW incomplete	Incomplete	Pond	November 2026
1	1995+96	2013+63	37.8	38.14	Incomplete	Incomplete	Upland	November 2026
1	2014+18	2014+32	38.15	38.15	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	2023+84	2024+36	38.33	38.34	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2036+11	2036+11	38.56	38.56	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2037+45	2037+84	38.59	38.60	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2047+43	2047+84	38.78	38.78	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2053+30	2053+30	38.89	38.89	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2057+15	2057+41	38.96	38.97	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2071+30	2071+45	39.23	39.23	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2075+68	2075+68	39.31	39.31	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2078+06	2078+15	39.36	39.36	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2082+53	2082+53	39.44	39.44	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2093+93	2093+93	39.66	39.66	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2126+89	2131+55	40.28	40.37	Incomplete	Incomplete	Upland	November 2026
1	2131+55	2140+82	40.37	40.55	Incomplete	Incomplete	Upland	November 2026
1	2140+82	2145+86	40.55	40.64	Incomplete	Incomplete	Upland	November 2026
1	2145+86	2151+48	40.64	40.75	Incomplete	Incomplete	Upland	November 2026
1	2167+07	2167+07	41.04	41.04	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2188+15	2188+15	41.44	41.44	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2190+47	2190+47	41.49	41.49	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2198+01	2198+01	41.63	41.63	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2214+90	2214+90	41.95	41.95	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2220+61	2220+86	42.06	42.06	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	2220+82	2231+95	42.06	42.27	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
1	2251+74	2251+74	42.65	42.65	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2273+21	2273+21	43.05	43.05	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2285+07	2285+07	43.28	43.28	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2261+03	2267+14	42.82	42.94	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
1	2305+30	230551.00	43.66	43.66	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2331+00	2331+44	44.15	44.16	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2341+21	2341+21	44.34	44.34	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2356+71	2356+71	44.63	44.63	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2360+69	2360+69	44.71	44.71	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2365+13	2365+13	44.79	44.79	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2378+95	2378+95	45.06	45.06	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2383+52	2383+52	45.14	45.14	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2399+79	2413+39	45.45	45.71	Incomplete	Incomplete	Upland	November 2026
1	2408+62	2408+62	45.62	45.62	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1			46.00	0.00	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2439+81	2439+81	46.21	46.21	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1			46.20	0.00	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2448+26	2448+26	46.37	46.37	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2457+93	2458+08	46.55	46.55	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	2475+30	2475+30	46.88	46.88	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2491+35	2495+23	47.18	47.26	Incomplete	Incomplete	Upland	November 2026
1	2495+23	2502+15	47.26	47.39	Incomplete	Incomplete	Upland	November 2026
1	2514+03	2514+03	47.61	47.61	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2520+05	2520+05	47.73	47.73	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2529+55	2529+55	47.91	47.91	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2533+54	2533+54	47.98	47.98	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2541+91	2541+91	48.14	48.14	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2545+85	2556+25	48.22	48.41	Incomplete	Incomplete	Upland	November 2026
1	2563+83	2563+83	48.56	48.56	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2566+75	2573+65	48.61	48.74	Incomplete	Incomplete	Upland	November 2026
1	2573+65	2593+62	48.74	49.12	Incomplete	Incomplete	Upland	November 2026
1	2597+60	2597+60	49.20	49.20	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2609+15	2609+15	49.42	49.42	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2614+86	2614+86	49.52	49.52	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2641+49	2649+84	50.03	50.19	Incomplete	Incomplete	Upland	November 2026
1	2650+33	2652+39	50.2	50.23	Incomplete	Incomplete	Upland	November 2026
1	2652+39	2655+94	50.23	50.3	Incomplete	Incomplete	Upland	November 2026
1	2684+82	2685+27	50.85	50.86	Complete	Restored	Perennial	September 2026
1	2717+60	2727+62	51.47	51.66	Incomplete	Incomplete	Upland	November 2026
1	2727+62	2737+17	51.66	51.84	Incomplete	Incomplete	Upland	November 2026
1	2755+27	2755+27	52.18	52.18	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
1	2756+65	2759+92	52.21	52.27	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2767+78	2767+78	52.42	52.42	Incomplete	Incomplete	Intermittent	October 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	2782+05	2782+05	52.69	52.69	Incomplete	Incomplete	Upland	November 2026
1	2785+53	2793+81	52.76	52.91	Incomplete	Incomplete	Upland	November 2026
1	2803+68	2803+68	53.10	53.10	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2812+30	2812+50	53.26	53.29	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2823+18	2823+18	53.47	53.47	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2838+30	2838+30	53.76	53.76	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2835+36	2835+36	53.70	53.70	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2849+09	2849+09	53.96	53.96	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2849+09	2849+09	53.96	53.96	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2888+03	2888+03	54.70	54.70	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2894+31	2894+31	54.82	54.82	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2906+96	2907+37	55.06	55.06	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2920+46	2920+84	55.31	55.32	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2935+99	2936+61	55.61	55.62	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2961+45	2961+45	56.09	56.09	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2963+20	2963+70	56.12	56.13	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2972+01	2972+47	56.29	56.30	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	2988+94	2988+94	56.61	56.61	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2990+71	2991+01	56.64	56.65	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	2992+79	2994+37	56.68	56.71	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	2993+76	2993+76	56.70	56.70	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
1	2998+74	2998+74	56.79	56.79	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	3006+64	3026+10	56.94	57.31	Incomplete	Incomplete	Upland	November 2026
1	3022+78	3022+78	57.25	57.25	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	3025+44	3025+44	57.30	57.30	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	3036+00	3036+00	57.50	57.50	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	3057+12	3057+12	57.90	57.90	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
1	3075+74	3076+05	58.25	58.25	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	3087+02	3087+02	58.47	58.47	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
1	3097+51	3097+51	58.66	58.66	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	3110+67	3110+67	58.91	58.91	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
1	3128+55	3141+06	59.25	59.49	Incomplete	Incomplete	Upland	November 2026
1	3141+06	3145+04	59.49	59.57	Incomplete	Incomplete	Upland	November 2026
1	3145+04	3151+24	59.57	59.68	Incomplete	Incomplete	Upland	November 2026
1	3151+93	3154+50	59.7	59.74	Incomplete	Incomplete	Upland	November 2026
Spread Break 1-2								
2	3176+80	3196+01	60.17	60.53	Complete	Restored	Upland	June 2026
2	3189+90	3192+00	60.41	60.45	Complete	Restored	Upland	June 2026
2	3205+35	3205+35	60.71	60.71	Complete	Restored	Perennial	June 2026
2	3205+35	3205+35	60.71	60.71	Complete	Restored	Upland	June 2026
2	3211+48	3211+48	60.82	60.82	Complete	Restored	Perennial	June 2026
2	3218+72	3218+72	60.96	60.96	Complete	Restored	Intermittent	June 2026
2	3232+28	3232+28	61.22	61.22	Complete	Restored	Ephemeral	June 2026
2	3225+83	3225+83	61.10	61.10	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3226+33	3226+58	61.10	61.11	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	3263+09	3263+34	61.80	61.80	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3290+59	3290+75	62.32	62.32	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3305+46	3305+46	62.60	62.60	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3309+50	3309+50	62.68	62.68	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3314+15	3314+15	62.77	62.77	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3322+50	3322+50	62.93	62.93	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3332+00	3332+00	63.11	63.11	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3359+78	3359+78	63.63	63.63	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3371+76	3371+83	63.86	63.86	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3375+71	3375+71	63.93	63.93	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3379+89	3379+89	64.01	64.01	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3388+58	3388+58	64.18	64.18	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3399+75	3399+75	64.39	64.39	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3402+77	3402+77	64.45	64.45	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3407+77	3407+77	64.54	64.54	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3404+14	3404+14	64.47	64.47	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3428+50	3428+50	64.93	64.93	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3433+50	3433+50	65.03	65.03	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3436+37	3436+37	65.08	65.08	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3438+98	3438+98	65.13	65.13	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	3440+18	3440+18	65.15	65.15	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3466+12	3466+12	65.65	65.65	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3470+50	3470+50	65.73	65.73	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3473+50	3473+50	65.79	65.79	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3475+00	3475+00	65.81	65.81	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3494+74	3496+94	66.19	66.23	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
2	3500+07	3500+07	66.29	66.29	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3496+94	3500+84	66.23	66.3	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
2	3500+84	3513+01	66.3	66.53	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
2	3513+01	3550+51	66.53	67.24	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
2	3521+76	3521+76	66.70	67.00	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
2	3564+52	3570+71	67.51	67.63	Resource restored, ROW incomplete	Incomplete	Upland	November 2026
2	3581+19	3581+19	67.83	67.83	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3581+41	3581+41	67.83	67.83	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3582+50	3582+50	67.85	67.85	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3579+50	3579+50	67.79	67.79	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3582+61	3582+61	67.85	67.85	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3591+29	3591+29	68.02	68.02	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3602+06	3602+06	68.22	68.22	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3611+89	3612+47	68.41	68.42	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	3627+00	3627+00	68.69	68.69	Resource restored, ROW incomplete	Restored	Ephemeral	November 2026
2	3634+00	3634+00	68.83	68.83	Resource restored, ROW incomplete	Restored	Perennial	November 2026
2	3640+03	3640+03	68.94	68.94	Resource restored, ROW incomplete	Restored	Ephemeral	November 2026
2	3640+90	3640+90	68.96	68.96	Resource restored, ROW incomplete	Restored	Intermittent	November 2026
2	3679+89	3679+89	69.69	69.69	Resource restored, ROW incomplete	Restored	Perennial	November 2026
2	3679+90	3679+90	69.70	69.70	Resource restored, ROW incomplete	Restored	Perennial	November 2026
2	3699+25	3699+25	70.06	70.06	Complete	Restored	Ephemeral	August 2026
2	3699+75	3699+75	70.07	70.07	Complete	Restored	Intermittent	August 2026
2	3700+00	3700+00	70.08	70.08	Complete	Restored	Intermittent	August 2026
2	3700+60	3700+60	70.09	70.09	Complete	Restored	Intermittent	August 2026
2	3709+14	3709+14	70.25	70.25	Complete	Restored	Perennial	August 2026
2	3720+48	3720+48	70.46	70.46	Complete	Restored	Perennial	August 2026
2	3729+25	3729+25	70.63	70.63	Complete	Restored	Intermittent	August 2026
2	3727+25	3727+25	70.59	70.59	Complete	Restored	Intermittent	August 2026
2	3737+47	3737+47	70.79	70.79	Complete	Restored	Perennial	August 2026
2	3741+00	3741+00	70.85	70.85	Complete	Restored	Perennial	August 2026
2	3744+50	3744+50	70.92	70.92	Complete	Restored	Intermittent	August 2026
2	3744+46	3744+46	70.92	70.92	Complete	Restored	Perennial	August 2026
2	3767+00	3767+00	71.34	71.34	Complete	Restored	Ephemeral	August 2026
2	3771+17	3771+17	71.42	71.42	Complete	Restored	Ephemeral	August 2026
2	3769+00	3769+00	71.38	71.38	Complete	Restored	Ephemeral	September 2026
2	3771+15	3771+15	71.42	71.42	Complete	Restored	Intermittent	September 2026
2	3776+47	3776+73	71.52	71.53	Complete	Restored	Perennial	September 2026
2	3806+50	3806+50	72.09	72.09	Resource restored, ROW incomplete	Incomplete	Pond	November 2026
2	3811+31	3811+31	72.18	72.18	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3811+92	3811+92	72.20	72.20	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	3812+50	3812+50	72.21	72.21	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3813+54	3813+54	72.23	72.23	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3838+93	3838+93	72.71	72.71	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3840+42	3840+42	72.74	72.74	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3840+85	3840+85	72.74	72.74	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3840+97	3840+97	72.75	72.75	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	3841+09	3841+54	72.75	72.76	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3847+50	3847+50	72.87	72.87	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3846+25	3846+25	72.85	72.85	Complete	Restored	Intermittent	August 2026
2	3852+00	3852+00	72.95	72.95	Complete	Restored	Intermittent	August 2026
2	3853+00	3853+00	72.97	72.97	Complete	Restored	Intermittent	August 2026
2	3864+52	3864+52	73.19	73.19	Complete	Restored	Intermittent	August 2026
2	3873+21	3873+21	73.36	73.36	Complete	Restored	Ephemeral	August 2026
2	3873+63	3873+63	73.36	73.36	Complete	Restored	Ephemeral	August 2026
2	3873+25	3873+25	73.36	73.36	Complete	Restored	Perennial	August 2026
2	3873+25	3873+25	73.36	73.36	Complete	Restored	Perennial	August 2026
2	3879+50	3879+50	73.48	73.48	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3883+16	3883+16	73.54	73.54	Complete	Restored	Ephemeral	July 2026
2	3881+01	3881+10	73.50	73.51	Complete	Restored	Perennial	July 2026
2	3884+75	3884+75	73.57	73.57	Complete	Restored	Ephemeral	July 2026
2	3893+53	3893+53	73.74	73.74	Complete	Restored	Intermittent	July 2026
2	3896+50	3896+50	73.80	73.80	Complete	Restored	Intermittent	July 2026
2	3912+50	3912+50	74.10	74.17	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3916+83	3916+98	74.18	74.19	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	3919+65	3919+65	74.24	74.24	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3920+47	3920+47	74.25	74.25	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	3930+50	3930+50	74.44	74.44	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3930+91	3930+91	74.45	74.45	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3930+50	3930+50	74.44	74.44	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3943+61	3943+61	74.69	74.69	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	3962+25	3962+25	75.04	75.04	Complete	Restored	Ephemeral	August 2026
2	3965+50	3965+50	75.10	75.10	Complete	Restored	Ephemeral	August 2026
2	3988+87	3988+87	75.55	75.55	Complete	Restored	Perennial	June 2026
2	4007+00	4007+00	75.89	75.89	Complete	Restored	Perennial	June 2026
2	4025+75	4025+75	76.25	76.25	Complete	Restored	Pond	July 2026
2	4045+03	4045+03	76.61	76.61	Complete	Restored	Perennial	June 2026
2	4045+34	4045+34	76.62	76.62	Complete	Restored	Perennial	June 2026
2	4052+31	4052+31	76.75	76.75	Complete	Restored	Perennial	June 2026
2	4059+30	4059+39	76.88	76.88	Complete	Restored	Perennial	June 2026
2	4079+45	4079+45	77.26	77.26	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	4081+61	4081+61	77.30	77.30	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	4089+02	4089+02	77.44	77.44	Complete	Restored	Ephemeral	August 2026
2	4094+50	4094+50	77.55	77.55	Complete	Restored	Pond	August 2026
2	4105+86	4105+86	77.76	77.76	Complete	Restored	Perennial	August 2026
2	4143+50	4143+50	78.48	78.48	Complete	Restored	Perennial	August 2026
2	4147+28	4147+28	78.55	78.55	Complete	Restored	Ephemeral	August 2026
2	4147+50	4147+50	78.55	78.55	Complete	Restored	Intermittent	August 2026
2	4145+25	4145+25	78.51	78.51	Complete	Restored	Perennial	August 2026
2	4147+50	4147+50	78.55	78.55	Complete	Restored	Perennial	August 2026
2	4145+25	4145+25	78.51	78.51	Complete	Restored	Perennial	August 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	4165+80	4165+80	78.90	78.90	Complete	Restored	Perennial	September 2026
2	4186+00	4186+00	79.28	79.28	Complete	Restored	Perennial	September 2026
2	4189+19	4189+38	79.34	79.34	Complete	Restored	Perennial	August 2026
2	4232+56	4232+56	80.16	80.16	Complete	Restored	Perennial	August 2026
2	4236+00	4236+00	80.23	80.23	Complete	Restored	Perennial	August 2026
2	4256+78	4256+78	80.62	80.62	Complete	Restored	Ephemeral	August 2026
2	4279+50	4279+50	81.05	81.05	Complete	Restored	Ephemeral	August 2026
2	4279+50	4279+50	81.05	81.05	Complete	Restored	Ephemeral	August 2026
2	4285+00	4285+00	81.16	81.16	Complete	Restored	Pond	August 2026
2	4265+81	4265+81	80.79	80.79	Complete	Restored	Perennial	July 2026
2	4266+01	4266+01	80.80	80.80	Complete	Restored	Perennial	July 2026
2	4266+90	4266+90	80.81	80.81	Complete	Restored	Perennial	July 2026
2	4271+26	4271+26	80.90	80.90	Complete	Restored	Perennial	July 2026
2	4285+30	4285+30	81.16	81.16	Complete	Restored	Perennial	July 2026
2	4283+90	4283+90	81.13	81.13	Complete	Restored	Perennial	June 2026
2	4291+00	4291+00	81.27	81.27	Complete	Restored	Intermittent	June 2026
2	4306+18	4306+18	81.56	81.56	Complete	Restored	Perennial	July 2026
2	4311+85	4311+85	81.66	81.66	Complete	Restored	Perennial	June 2026
2	4311+50	4311+50	81.66	81.66	Complete	Restored	Perennial	June 2026
2	4320+44	4320+44	81.83	81.83	Complete	Restored	Intermittent	June 2026
2	4353+00	4353+00	82.44	82.44	Complete	Restored	Intermittent	June 2026
2	4352+80	4352+80	82.44	82.44	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	4359+33	4359+33	82.56	82.56	Complete	Restored	Perennial	June 2026
2	4391+03	4391+03	83.16	83.16	Complete	Restored	Perennial	June 2026
2	4404+44	4404+44	83.42	83.42	Complete	Restored	Perennial	June 2026
2	4419+25	4419+25	83.70	83.70	Complete	Restored	Perennial	July 2026
2	4421+71	4421+71	83.74	83.74	Complete	Restored	Perennial	June 2026
2	4422+40	4422+40	83.76	83.76	Complete	Restored	Perennial	July 2026
2	4440+37	4440+37	84.10	84.10	Complete	Restored	Perennial	June 2026
2	4440+10	4440+10	84.09	84.09	Complete	Restored	Perennial	June 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	4443+00	4443+00	84.15	84.15	Complete	Restored	Ephemeral	July 2026
2	4455+50	4455+50	84.38	84.38	Complete	Restored	Intermittent	July 2026
2	4460+15	4460+15	84.47	84.47	Complete	Restored	Perennial	July 2026
2	4460+81	4466+04	84.49	84.58	Complete	Restored	Pond	June 2026
2	4466+25	4466+25	84.59	84.59	Complete	Restored	Ephemeral	July 2026
2	4484+40	4484+40	84.93	84.93	Complete	Restored	Ephemeral	May 2026
2	4498+22	4498+22	85.19	85.19	Complete	Restored	Intermittent	May 2026
2	4503+47	4503+47	85.29	85.29	Complete	Restored	Intermittent	May 2026
2	4509+48	4509+48	85.41	85.41	Complete	Restored	Intermittent	May 2026
2	4539+17	4539+17	85.97	85.97	Complete	Restored	Intermittent	July 2026
2	4539+17	4539+17	85.97	85.97	Complete	Restored	Intermittent	May 2026
2	4542+75	4542+75	86.04	86.04	Complete	Restored	Ephemeral	July 2026
2	4576+70	4576+70	86.68	86.68	Complete	Restored	Perennial	May 2026
2	4576+25	4576+25	86.67	86.67	Complete	Restored	Perennial	July 2026
2	4577+00	4577+00	86.69	86.69	Complete	Restored	Perennial	May 2026
2	4587+63	4587+63	86.89	86.89	Complete	Restored	Perennial	May 2026
2	4608+13	4608+13	88.20	87.28	Complete	Restored	Intermittent	May 2026
2	4622+25	4622+25	87.54	87.54	Complete	Restored	Perennial	July 2026
2	4622+46	4622+46	87.55	87.55	Complete	Restored	Perennial	May 2026
2	4635+66	4635+66	87.80	87.80	Complete	Restored	Intermittent	May 2026
2	4830+00	4830+00	91.48	91.48	Complete	Restored	Intermittent	May 2026
2	4664+31	4664+31	88.34	88.34	Complete	Restored	Perennial	May 2026
2	4685+86	4686+79	88.75	88.76	Complete	Restored	Pond	May 2026
2	4728+53	4728+53	89.56	89.56	Complete	Restored	Perennial	May 2026
2	4730+75	4730+75	89.60	89.60	Complete	Restored	Ephemeral	June 2026
2	4242+70	4242+70	80.35	80.35	Complete	Restored	Intermittent	June 2026
2	4744+35	4744+35	89.86	89.86	Complete	Restored	Ephemeral	June 2026
2	4242+36	4242+36	80.35	80.35	Complete	Restored	Intermittent	June 2026
2	4742+79	4742+79	89.83	89.83	Complete	Restored	Intermittent	June 2026
2	4769+43	4770+03	90.33	90.34	Complete	Restored	Perennial	May 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	4795+25	4795+25	90.82	90.82	Complete	Restored	Ephemeral	June 2026
2	4795+18	4795+18	90.82	90.82	Complete	Restored	Intermittent	June 2026
2	4795+18	4795+18	90.82	90.82	Complete	Restored	Intermittent	June 2026
2	4794+98	4794+98	90.81	90.81	Complete	Restored	Intermittent	June 2026
2	4806+73	4806+73	91.04	91.04	Complete	Restored	Ephemeral	June 2026
2	4809+38	4809+38	91.09	91.09	Complete	Restored	Intermittent	June 2026
2	4814+25	4814+25	91.18	91.18	Complete	Restored	Perennial	May 2026
2	4835+35	4835+78	91.58	91.59	Complete	Restored	Perennial	May 2026
2	4857+71	4857+71	92.00	92.00	Complete	Restored	Intermittent	May 2026
2	4864+00	4864+00	92.12	92.12	Complete	Restored	Ephemeral	May 2026
2	4868+93	4868+93	92.21	92.21	Complete	Restored	Perennial	May 2026
2	4884+19	4884+19	92.50	92.50	Complete	Restored	Ephemeral	May 2026
2	4888+25	4888+25	92.58	92.58	Complete	Restored	Ephemeral	May 2026
2	4888+26	4888+26	92.58	92.58	Complete	Restored	Perennial	May 2026
2	4902+00	4902+00	92.84	92.84	Complete	Restored	Ephemeral	May 2026
2	4902+18	4902+18	92.84	92.84	Complete	Restored	Perennial	May 2026
2	4908+75	4908+75	92.97	92.97	Complete	Restored	Ephemeral	May 2026
2	4915+00	4915+00	93.09	93.09	Complete	Restored	Pond	May 2026
2	4928+25	4928+25	93.34	93.34	Complete	Restored	Intermittent	May 2026
2	4928+50	4928+50	93.34	93.34	Complete	Restored	Perennial	May 2026
2	4928+74	4929+00	93.35	93.35	Complete	Restored	Perennial	May 2026
2	4956+90	4956+90	93.88	93.88	Complete	Restored	Perennial	May 2026
2	4980+50	4980+50	94.33	94.33	Complete	Restored	Perennial	May 2026
2	4980+50	4980+50	94.33	94.33	Complete	Restored	Perennial	May 2026
2	4980+50	4980+50	94.33	94.33	Complete	Restored	Perennial	May 2026
2	4973+51	4973+51	94.20	94.20	Complete	Restored	Ephemeral	May 2026
2	4978+14	4978+14	94.28	94.28	Complete	Restored	Ephemeral	May 2026
2	4978+50	4978+50	94.29	94.29	Complete	Restored	Intermittent	May 2026
2	4978+75	4978+75	94.29	94.29	Complete	Restored	Perennial	May 2026
2	4985+36	4985+53	94.42	94.42	Complete	Restored	Perennial	May 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	4996+48	4996+59	94.63	94.63	Complete	Restored	Intermittent	May 2026
2	5036+50	5036+50	95.39	95.39	Complete	Restored	Perennial	May 2026
2	5040+76	5040+76	95.47	95.47	Complete	Restored	Ephemeral	May 2026
2	5044+25	5044+39	95.54	95.54	Complete	Restored	Perennial	May 2026
2	5046+17	5046+17	95.57	95.57	Complete	Restored	Perennial	May 2026
2	5066+25	5066+25	95.95	95.95	Complete	Restored	Perennial	May 2026
2	5103+01	5103+01	96.65	96.65	Complete	Restored	Ephemeral	May 2026
2	5110+75	5110+75	96.79	96.79	Complete	Restored	Perennial	September 2026
2	5125+26	5125+26	97.07	97.07	Complete	Restored	Perennial	May 2026
2	5143+87	5175+01	97.42	98.01	Complete	Restored	Upland	May 2026
2	5194+24	5194+24	98.38	98.38	Complete	Restored	Ephemeral	August 2026
2	5203+41	5207+15	98.55	98.62	Complete	Restored	Upland	August 2026
2	5207+15	5210+64	98.62	98.69	Complete	Restored	Upland	August 2026
2	5210+64	5213+50	98.69	98.74	Complete	Restored	Upland	August 2026
2	5229+78	5229+78	99.05	99.05	Complete	Restored	Perennial	August 2026
2	5233+55	5233+55	99.12	99.12	Complete	Restored	Ephemeral	August 2026
2	5233+70	5233+70	99.12	99.12	Complete	Restored	Ephemeral	August 2026
2	5233+25	5233+25	99.11	99.11	Complete	Restored	Perennial	August 2026
2	5235+50	5235+50	99.16	99.16	Complete	Restored	Intermittent	August 2026
2	5239+66	5240+67	99.24	99.26	Complete	Restored	Pond	August 2026
2	5283+00	5283+00	100.06	100.06	Complete	Restored	Ephemeral	August 2026
2	5284+79	5285+01	100.09	100.09	Complete	Restored	Perennial	August 2026
2	5283+00	5283+00	100.06	100.06	Complete	Restored	Perennial	August 2026
2	5289+73	5289+73	100.18	100.18	Complete	Restored	Perennial	August 2026
2	5310+92	5310+92	100.59	100.59	Complete	Restored	Perennial	August 2026
2	5318+00	5318+00	100.72	100.72	Complete	Restored	Ephemeral	August 2026
2	5333+35	5333+35	101.01	101.01	Complete	Restored	Perennial	August 2026
2	5338+39	5338+39	101.11	101.11	Complete	Restored	Intermittent	August 2026
2	5350+90	5350+90	101.34	101.34	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	5365+72	5365+72	101.62	101.62	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5384+92	5385+90	101.99	102.01	Resource restored, ROW incomplete	Incomplete	Perennial	October 2026
2	5409+90	5409+90	102.46	102.46	Resource restored, ROW incomplete	Incomplete	Pond	October 2026
2	5409+31	5409+31	102.45	102.45	Resource restored, ROW incomplete	Incomplete	Perennial	October 2026
2	5414+60	5414+60	102.55	102.55	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5419+00	5419+00	102.63	102.63	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5412+00	5412+00	102.50	102.50	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5426+00	5426+00	102.77	102.77	Resource restored, ROW incomplete	Incomplete	Pond	October 2026
2	5437+17	5437+17	102.98	102.98	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5439+80	5439+80	103.03	103.03	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5452+57	5452+57	103.27	103.27	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5468+54	5468+54	103.57	103.57	Resource restored, ROW incomplete	Incomplete	Perennial	October 2026
2	5473+50	5473+50	103.66	103.66	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5530+75	5530+75	104.75	104.75	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5531+43	5531+43	104.76	104.76	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5534+25	5534+25	104.82	104.82	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5533+15	5533+46	104.79	104.80	Resource restored, ROW incomplete	Incomplete	Perennial	October 2026
2	5540+50	5540+50	104.93	104.93	Resource restored, ROW incomplete	Incomplete	Pond	October 2026
2	5556+54	5556+54	105.24	105.24	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5570+43	5571+09	105.50	105.51	Resource restored, ROW incomplete	Incomplete	Perennial	October 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	5592+15	5592+15	105.91	105.91	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5615+96	5615+96	106.36	106.36	Resource restored, ROW incomplete	Incomplete	Intermittent	October 2026
2	5622+97	5622+97	106.50	106.50	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5625+09	5625+09	106.54	106.54	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5625+66	5625+66	106.55	106.55	Resource restored, ROW incomplete	Incomplete	Ephemeral	October 2026
2	5626+66	5626+66	106.57	106.57	Complete	Restored	Perennial	September 2026
2	5633+75	5633+75	106.70	106.70	Complete	Restored	Ephemeral	September 2026
2	5636+50	5636+50	106.75	106.75	Complete	Restored	Perennial	September 2026
2	5641+77	5641+77	106.85	106.85	Complete	Restored	Perennial	September 2026
2	5653+58	5653+58	107.08	107.08	Complete	Restored	Intermittent	September 2026
2	5662+47	5662+47	107.24	107.24	Complete	Restored	Intermittent	September 2026
2	5683+37	5683+37	107.64	107.64	Complete	Restored	Ephemeral	September 2026
2	5683+50	5683+50	107.64	107.64	Complete	Restored	Perennial	September 2026
2	5691+85	5691+85	107.80	107.80	Complete	Restored	Ephemeral	September 2026
2	5698+28	5698+28	107.92	107.92	Complete	Restored	Perennial	September 2026
2	5710+72	5710+72	108.16	108.16	Complete	Restored	Intermittent	September 2026
2	5735+42	5735+42	108.63	108.63	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	5766+01	5766+01	109.20	109.20	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	5766+30	5766+38	109.21	109.21	Complete	Restored	Perennial	September 2026
2	5778+79	5778+79	109.45	109.45	Complete	Restored	Perennial	September 2026
2	5791+00	5791+00	109.68	109.68	Complete	Restored	Ephemeral	September 2026
2	5790+92	5790+92	109.68	109.68	Complete	Restored	Ephemeral	September 2026
2	5791+23	5791+23	109.68	109.68	Complete	Restored	Intermittent	September 2026
2	5800+25	5800+25	109.85	109.85	Complete	Restored	Intermittent	September 2026
2	5801+03	5801+03	109.87	109.87	Complete	Restored	Intermittent	August 2026
2	5813+24	5813+24	110.10	110.10	Complete	Restored	Intermittent	September 2026
2	5816+40	5816+40	110.16	110.16	Complete	Restored	Intermittent	September 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	5816+40	5816+40	110.16	110.16	Complete	Restored	Ephemeral	September 2026
2	5816+44	5816+44	110.16	110.16	Complete	Restored	Intermittent	September 2026
2	5839+75	5839+75	110.60	110.60	Complete	Restored	Ephemeral	September 2026
2	5864+39	5864+39	111.07	111.07	Complete	Restored	Ephemeral	September 2026
2	5862+75	5862+75	111.04	111.04	Complete	Restored	Ephemeral	September 2026
2	5899+25	5899+25	111.73	111.73	Complete	Restored	Ephemeral	September 2026
2	5909+67	5909+67	111.93	111.93	Complete	Restored	Perennial	September 2026
2	5930+21	5930+43	112.31	112.32	Complete	Restored	Perennial	September 2026
2	5936+75	5936+75	112.44	112.44	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	5941+29	5942+12	112.52	112.54	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	5943+25	5943+25	112.56	112.56	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	5949+22	5949+34	112.67	112.68	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	5962+25	5962+25	112.92	112.92	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	5974+38	5974+77	113.15	113.16	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	5982+67	5983+22	113.31	113.32	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	5993+69	5994+20	113.52	113.53	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6002+19	6002+19	113.68	113.68	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6012+05	6012+05	113.86	113.86	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	6025+50	6025+50	114.12	114.12	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6025+24	6025+24	114.11	114.11	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6027+00	6027+00	114.15	114.15	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6028+96	6028+96	114.18	114.18	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6032+88	6032+88	114.26	114.26	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	6037+76	6038+49	114.35	114.37	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6056+74	6056+74	114.71	114.71	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6080+59	6080+59	115.16	115.16	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6086+45	6086+45	115.27	115.27	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6114+24	6114+24	115.80	115.80	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6125+79	6125+79	116.02	116.02	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6130+39	6130+39	116.11	116.11	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6133+78	6133+78	116.17	116.17	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6144+19	6149+08	116.37	116.46	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6156+30	6156+30	116.60	116.60	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	6158+59	6158+59	116.64	116.64	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	6173+66	6173+76	116.93	116.93	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6177+74	6177+74	117.00	117.00	Resource restored, ROW incomplete	Incomplete	Intermittent	November 2026
2	6186+43	6186+43	117.17	117.17	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6186+10	6186+10	117.16	117.16	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6185+20	6185+20	117.14	117.14	Resource restored, ROW incomplete	Incomplete	Ephemeral	November 2026
2	6189+27	6189+27	117.22	117.22	Complete	Restored	Perennial	July 2026
2	6193+50	6193+50	117.30	117.30	Complete	Restored	Intermittent	July 2026
2	6193+90	6193+90	117.31	117.31	Complete	Restored	Perennial	July 2026
2	6205+12	6205+12	117.52	117.52	Complete	Restored	Ephemeral	July 2026
2	6204+30	6204+30	117.51	117.51	Complete	Restored	Ephemeral	July 2026
2	6206+50	6206+50	117.55	117.55	Complete	Restored	Ephemeral	July 2026

Spread	Begin Sta.	End Sta.	Begin MP	End MP	Restoration Status	Construction Status	Type	Projected Seeding Completion (Actual Completion Shaded)
2	6207+27	6207+27	117.56	117.56	Complete	Restored	Ephemeral	July 2026
2	6208+60	6208+60	117.59	117.59	Complete	Restored	Intermittent	July 2026
2	6217+93	6217+93	117.76	117.76	Complete	Restored	Ephemeral	July 2026
2	6217+56	6217+56	117.76	117.76	Resource restored, ROW incomplete	Incomplete	Perennial	November 2026
2	6218+94	6218+94	117.78	117.78	Complete	Restored	Ephemeral	June 2026
2	6288+90	6288+90	119.11	119.11	Complete	Restored	Ephemeral	June 2026
2	6290+96	6290+96	119.15	119.15	Complete	Restored	Ephemeral	July 2026
2	6290+70	6290+70	119.14	119.14	Complete	Restored	Intermittent	July 2026
2	6294+53	6294+53	119.21	119.21	Complete	Restored	Intermittent	July 2026
2	6305+70	6305+92	119.43	119.43	Complete	Restored	Perennial	June 2026
2	6306+50	6306+50	119.44	119.44	Complete	Restored	Ephemeral	June 2026
2	6311+79	6311+79	119.54	119.54	Complete	Restored	Ephemeral	June 2026
2	6348+67	6348+67	120.24	120.24	Complete	Restored	Ephemeral	June 2026
2	6375+50	6375+50	120.75	120.75	Complete	Restored	Ephemeral	June 2026
2	6377+75	6377+75	120.79	120.79	Complete	Restored	Ephemeral	June 2026
2	6381+09	6381+09	120.85	120.85	Complete	Restored	Ephemeral	June 2026
2	6381+52	6381+52	120.86	120.86	Complete	Restored	Ephemeral	June 2026
2	6381+30	6381+30	120.86	120.86	Complete	Restored	Ephemeral	June 2026
2	6383+29	6383+29	120.90	120.90	Complete	Restored	Ephemeral	June 2026
2	6385+34	6385+34	120.93	120.93	Complete	Restored	Ephemeral	June 2026
2	6385+58	6385+58	120.94	120.94	Complete	Restored	Ephemeral	June 2026
2	6389+42	6389+42	121.01	121.01	Complete	Restored	Ephemeral	June 2026
2	6438+49	6449+14	121.94	122.14	Complete	Restored	Perennial	June 2026

ATTACHMENT D

East Tennessee Natural Gas, LLC
Ridgeline Expansion Project
Landowner Issues

Tract	MP	Current Status	Plan for Resolution	Expected Resolution Date
TN-SM-290.03	23.7	New septic system to be installed. Awaiting Tennessee Department of Environment and Conservation ("TDEC") approval prior to installation.	East Tennessee to install new septic system, following soil test and TDEC approval.	11/27/2026
TN-JC-380	38.1	New septic system to be installed. Preliminary TDEC approval received; awaiting TDEC final approval prior to installation.	East Tennessee to install new septic system, following TDEC approval.	10/30/2026
TN-MR-734 & 734.01	106.15	Pond sample collected to evaluate oxygen levels due to fertilizer runoff; awating final labarotary results.	East Tennessee to remediate the pond based on final laboratory results and the recommendations.	10/23/2026
TN-MR-737	106.28	New septic system to be installed. Awaiting TDEC approval prior to installation.	East Tennessee to install new septic system, following soil test and TDEC approval.	11/13/2026
TN-MR-769.01- 770	108.38	New septic system to be installed. Awaiting TDEC approval prior to installation.	East Tennessee to install new septic system, following soil test and TDEC approval.	11/20/2026
TN-MR-779	109.5	New septic system to be installed. Awaiting TDEC approval prior to installation.	East Tennessee to install new septic system, following soil test and TDEC approval.	11/6/2026
